


# BOND PROJECTS UPDATE

ROADMAP OF THE PROGRESS OF 2015 BOND PROJECTS THAT TOOK PLACE OVER SUMMER 2016 AND BEYOND.  
PROJECTS ARE IN ORDER OF THE ESTIMATED COMPLETION DATE.  
ALL DATES ARE ESTIMATES AND ARE SUBJECT TO CHANGE AT ANY TIME.



JUNE 2016

**PHONE SYSTEM UPGRADE (VOIP)**  
DISTRICT-WIDE  
COMPLETED: JUN 2016



**ROBOTICS/ENGINEERING**  
REPURPOSE EXISTING M&O FACILITY  
COMPLETED: AUG 2016

JULY 2016



**FOOTBALL STADIUM PA SYSTEM**  
ENHANCE  
COMPLETED: AUG 2016

AUG 2016

**CAMPUS FIBER BACKBONE & CABLING**  
DISTRICT-WIDE  
COMPLETED: AUG 2016



**ROOFING**  
WESTLAKE HS, BARTON CREEK ES,  
VALLEY VIEW ES  
COMPLETED: AUG 2016

**HVAC RENOVATION**  
VALLEY VIEW ES  
COMPLETED: AUG 2016




**WINDOW REPLACEMENTS**  
WEST RIDGE MS  
YEAR 1 COMPLETED: AUG 2016

**CAFETERIA LIGHTING**  
HILL COUNTRY MS  
COMPLETED: AUG 2016



**EANES ELEMENTARY PARKING EXPANSION**  
IMPROVE TRAFFIC FLOW  
COMPLETED: AUG 2016



**TENNIS COURT RESURFACING**  
AT HILL COUNTRY & WEST RIDGE MS  
COMPLETED: AUG 2016




**SHRINER SITE PARKING EXPANSION**  
COMPLETED: AUG 2016



**EXISTING TRANSPORTATION FACILITY**  
RENOVATIONS/ADDITIONS  
START DATE: MAR 21  
ESTIMATED COMPLETION: DEC 31



**EXISTING SHRINER WAREHOUSE**  
RENOVATIONS/ADDITIONS  
START DATE: MAY 16  
ESTIMATED COMPLETION: OCT 31

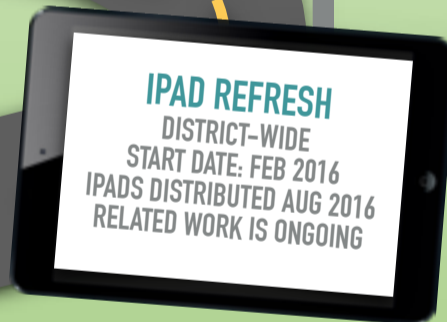

**IPAD REFRESH**  
DISTRICT-WIDE  
START DATE: FEB 2016  
IPADS DISTRIBUTED AUG 2016  
RELATED WORK IS ONGOING

DEC 2016



**DISTRICT OPERATIONS CENTER (DOC)**  
NEW BUILD TO HOUSE M&O, TECHNOLOGY,  
RENTALS & SAFETY  
START DATE: MAY 16  
ESTIMATED COMPLETION: DEC 31



**FINE ARTS ADDITIONS**  
RENOVATION/ADDITIONS FOR WEST RIDGE MS  
START DATE: JUN 6  
RENOVATED AREAS APPROX. COMPLETION AUG 19  
ESTIMATED COMPLETION: DEC 31  
  
ADDITION FOR HILL COUNTRY MS  
START DATE: SEP 15  
ESTIMATED COMPLETION: JAN 31, 2017

**ONGOING PROJECTS**  
**COMPUTER DESKTOP/LAPTOP REPLACEMENTS**  
DISTRICT-WIDE; START DATE: JAN 2016  
**EMERGING TECHNOLOGY**  
INCLUDES 3D PRINTERS, EMERGING TECH, ETC.  
DISTRICT-WIDE; START DATE: JUN 2015  
**REFURBISH WALLS, FLOORS, CEILINGS & OTHER SURFACES**  
DISTRICT-WIDE; START DATE: JUN  
WORK TO BE COMPLETED SUMMERS 2016/2017/2018  
**SECURITY CAMERA & ACCESS CONTROL**  
DISTRICT-WIDE; PHASE 1 30% COMPLETE

AUG 2016
